



TAYLORNW

NUID Piping Project Group 1 – Segment 2

Weekly Executive Summary


Week Ending February 14, 2025

PROJECT SCHEDULE – 3-WEEK LOOK AHEAD

	Contractor	Su	M	T	W	TH	F	Sa	Su	M	T	W	TH	F	Sa	Su	M	T	W	TH	F
A+B4:AT28+AT21+B4:B4:AT28	Notes	2/16	2/17	2/18	2/19	2/20	2/21	2/22	2/23	2/24	2/25	2/26	2/27	2/28	3/1	2/16	2/17	2/18	2/19	2/20	2/21
43 Lateral Excavation (WEST OF HWY 97)	TNW		■	■	■	■	■			■	■	■	■	■			■	■	■	■	■
53" Pipe Delivery	FERGUSON																				
53" Weld	TNW		■	■	■	■	■	■		■	■	■	■	■	■		■	■	■	■	■
43 lateral backfill			■	■	■	■	■			■	■	■	■	■	■		■	■	■	■	■
43-2 Turnouts 16x10 ISCO	ISCO																				
PRV	TNW																				
43-3 weld pipe	TNW																				
43-3 Excavate and backfill trench	TNW																				
43-5 Weld pipe	TNW											■	■	■							
43-5 10" under highway	TNW																				
43-5 Excavate and backfill trench	TNW											■	■	■							
Turnouts	TNW		■	■	■	■	■			■	■	■	■	■			■	■	■	■	■
restoration 43-2	TNW		■	■	■	■	■			■	■	■	■	■							
Hydrostatic testing (all turnouts must be complete)	tnw				■	■	■			■	■	■	■	■							



PROJECT WORK ACTIVITIES

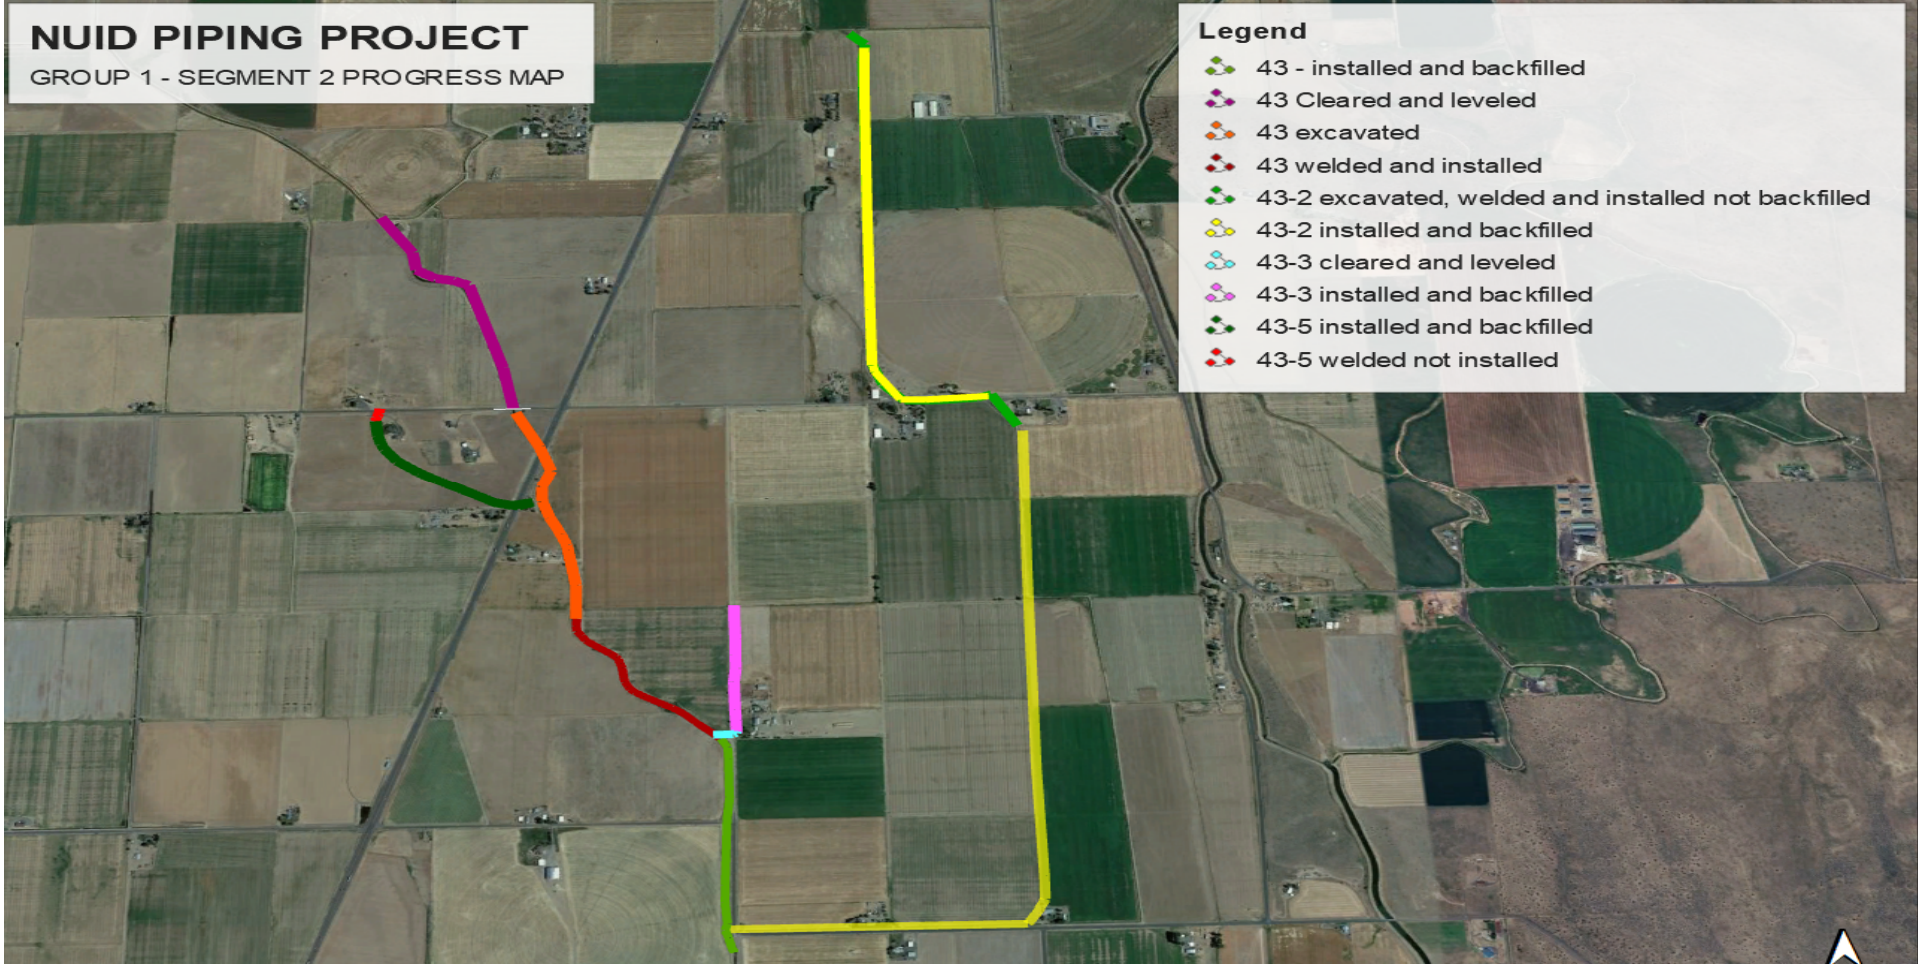


NUID Piping Project Group 1 – Segment 2



10-DAY WEATHER FORECAST

 Customize

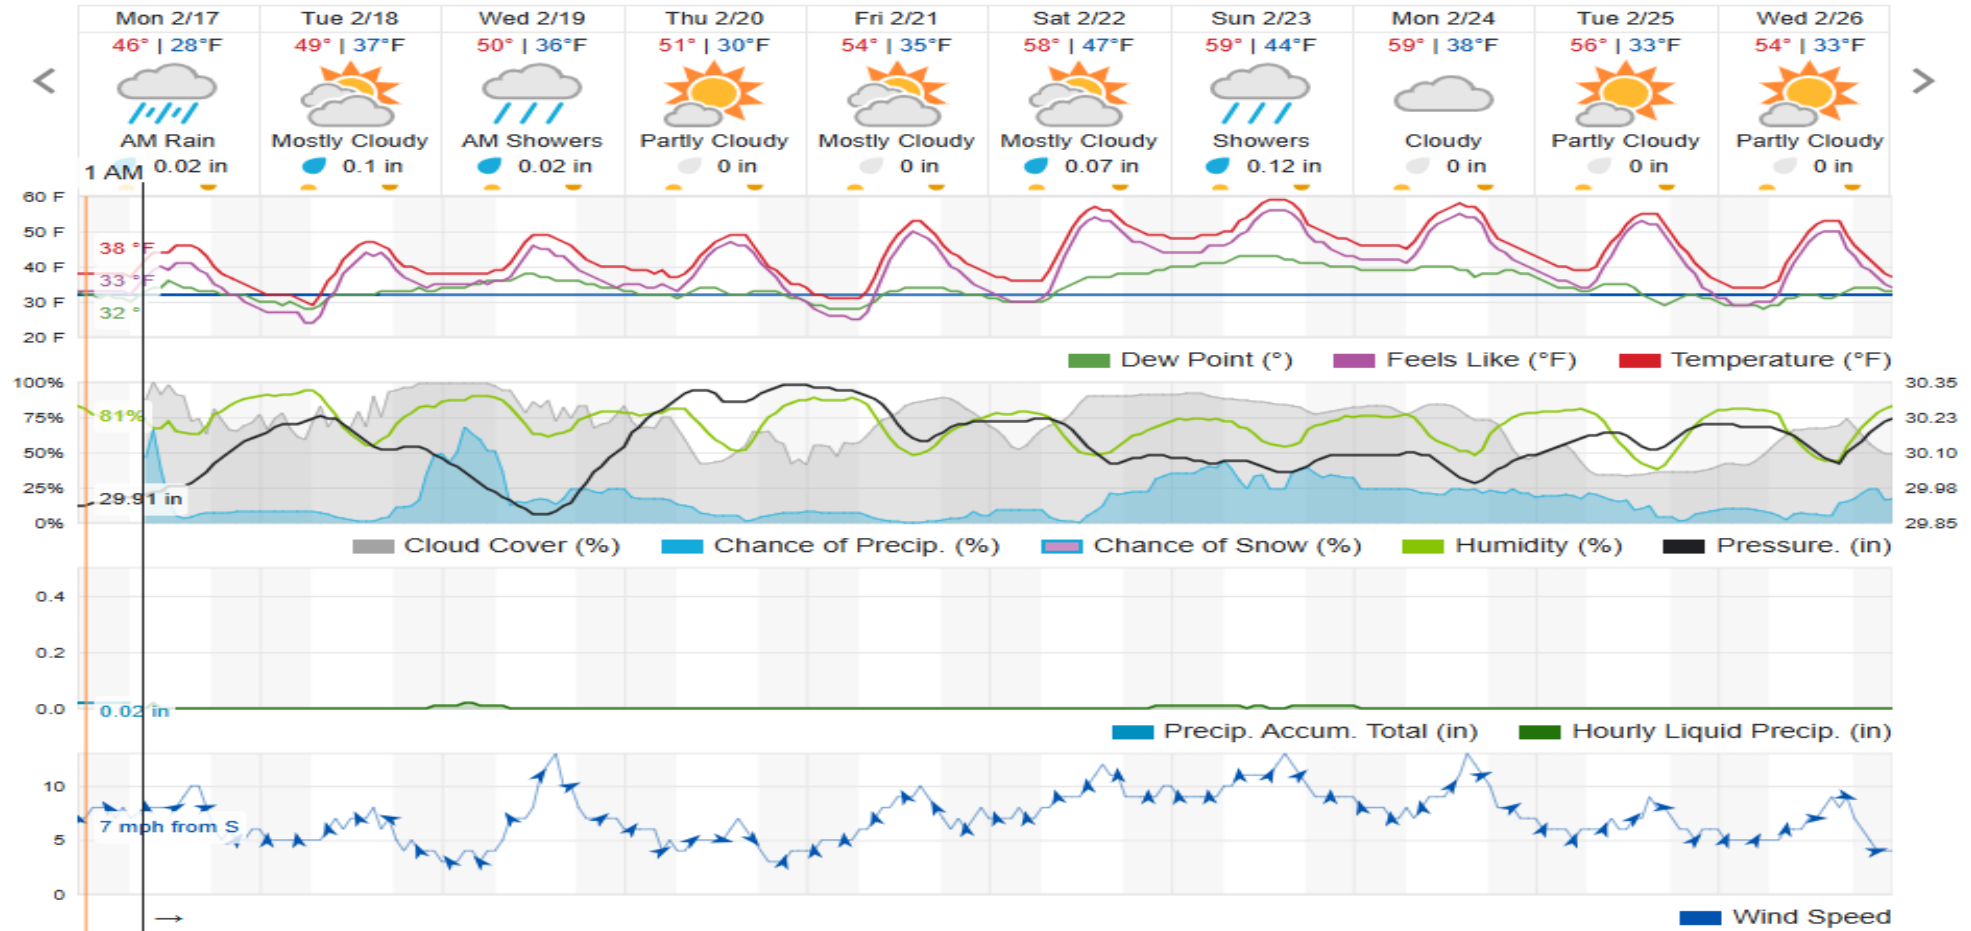

NUID Piping Project Group 1 – Segment 2



TAYLORNW

SAFETY

Hot Topics/Risks

- Welding machine facer, hot plate, and pinch points.
- Handling large pipe
- Overhead power lines
- Utility crossings
- Open trench
- Power from generator to large welding machine
- Soft haul roads
- Icy Conditions

Safety Documentation

Task Description	Start/Finish Date	Document
TNW Safety Plan	10/24/24	Safety Plan
Trenching	10/28/24 - On going	Pre task Plan
Welding HDPE	11/7/2024 - On going	Pre-Task Plan
Pipe Installation	11/15/2024 - On going	Pre-Task Plan
Traffic control	11/15/2024 - On going	Traffic Control Plan
Large pipe unloading	12/06/2024 – On Going	Pre-Task Plan
Backfill	12/9/2024 – On going	Pre-Task Plan
Grade work HWY 97	12/18/2024-1/18/2025	Pre-Task Plan
Night work on 97	1/8/2025- 1/30/2025	Pre-Task Plan
Casing install	1/9/2024 – 1/30/2025	Pre-Task Plan
Road Closures	1/27/2025 - On going	Pre-Task Plan

Incidents / Concerns

- N/A



QUALITY

Hot Topics/Risks

- Welding data logger
- Rain and bad weather
- Sick conditions
- Pulling pipe through casing

QA/QC Documentation

Task Description	QA/QC Representative	Date
Weld data log	TNW	Ongoing
Backfill proctor	Carlson testing	11/13/2024
Pipe bedding proctor	Carlson testing	11/13/2024
8" Bend back test	Kelley Hamby	11/19/2024
20" bend back test	Kelley Hamby	11/19/2024
Density Testing 43-2	Carlson testing	11/21/2024
16" Bend back test	Kevin Krew	11/22/2024
Density testing	Carlson testing	On going
63" Bend Back Test	Kevin Krew	On going
6" & 8" Bend back tests	Kelley Hamby	1/3/2025
6" bend back test	Kelley Hamby	1/09/2025
Density testing HWY 97	Carlson Testing	01/15/2025-01/25/2025

Look Ahead QA/QC

- Weld inspections, 63", 10", 6"
- Pipe inspections all week
- Turn out and ARV inspection all week



PROJECT PHOTOS



43 LATERAL WELD 63"



43 LATERAL WELD 63"



PROJECT PHOTOS



43-2 prv



43 EXCAVATE WEST OF 97

